


- **600 St. Peter (From Chartres To Royal)**

- Estimated Completion Date: Summer 2026
- Work currently completed and details if needed:
 - Sewer: 100%
 - Drainage: 100%
 - Water: 100%
 - Pavement: 95%
 - Sidewalks: 0%
- Roubion crews are ensuring the street is safe for pedestrian traffic by adding asphalt to sidewalks prior to fencing removal. Fencing will be removed by this weekend for the entire block with the exception of the intersection of Royal & St. Peter. That intersection should be completed by next week once the final concrete pour is complete.



- **1100 Decatur (From Gov. Nicholls To Ursulines)**
 - Estimated Completion Date: Summer 2026
 - Work currently completed and details if needed:
 - Sewer: 100%
 - Drainage: 100%
 - Water: 100%
 - Pavement: 95%
 - Sidewalks: 0%
 - Next week, crews will begin placing asphalt on the sidewalks to ensure site safety prior to fencing removal.

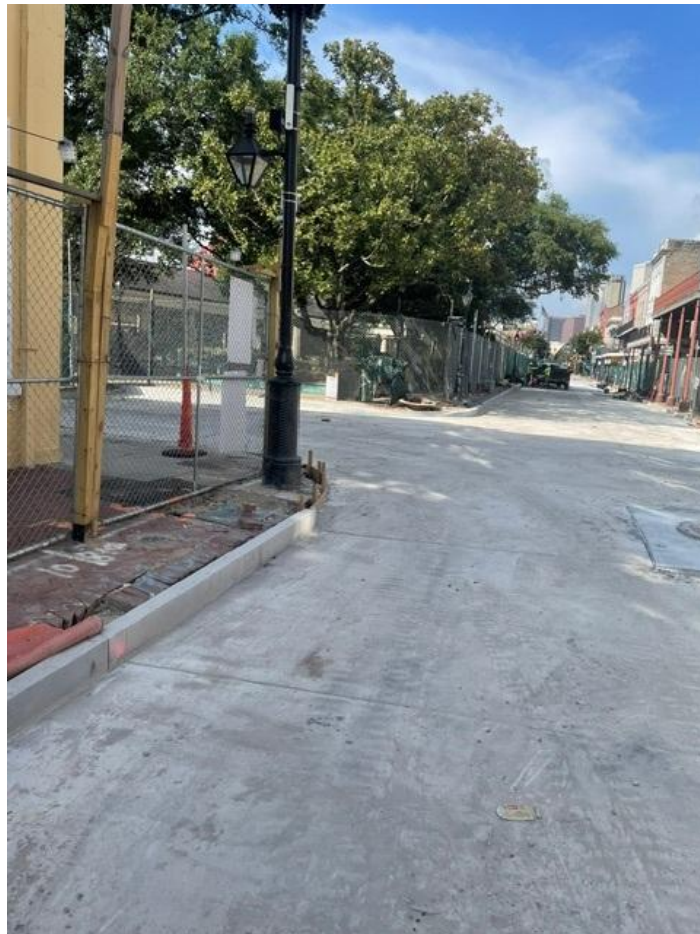

- **1000 Decatur (From Ursulines To St. Philip)**

- Estimated Completion Date: Fall 2026
- Work currently completed and details if needed:
 - Sewer: 100%
 - Drainage: 100%
 - Water: 100%
 - Pavement: 80%
 - Sidewalks: 0%
- Crews completed the final concrete pour for this phase of construction and mesh has been removed.



- **900 Decatur (From St. Philip To Dumaine)**

- Estimated Completion Date: Fall 2026
- Work currently completed and details if needed:
 - Sewer: 100%
 - Drainage: 90%
 - Water: 0%
 - Pavement: 0%
 - Sidewalks: 0%
- Crews have completed the tie in of temporary water services and crews have started water line installation for this block.



DELTA UTILITIES UPDATE

Provided by Delta Utilities on 6.30.2026

Delta's gas installation work in the **1200 block of Decatur Street** has been completed. Sidewalk restoration is currently underway, and street restoration will follow.

Delta also has sidewalk restoration work remaining on the riverside of the **1100 block of Decatur Street**, which will be coordinated with Joel.

Additionally, both street and sidewalk restoration activities have commenced on **French Market Place**.

Currently, Delta's subcontractor is projected to complete all restoration work by the **end of July**.
