



FRENCH QUARTER CONSTRUCTION UPDATE

600 St Peter St and 900-1100 Decatur St

Updated
October 27, 2026

600 ST. PETER

Chartres to Royal

ESTIMATED COMPLETION
COMPLETED

SEWER	100%
DRAINAGE	100%
WATER	100%
PAVEMENT	100%
SIDEWALKS	100%

CURRENT WORK

This block is complete and has been reopened to vehicular traffic.

1100 DECATUR

Gov. Nicholls to Ursulines

ESTIMATED COMPLETION
COMPLETED

SEWER	100%
DRAINAGE	100%
WATER	100%
PAVEMENT	100%
SIDEWALKS	100%

CURRENT WORK

This block is complete and continues to be open for pedestrian traffic.

1000 DECATUR

Ursulines to St. Philip

ESTIMATED COMPLETION
Fall 2026

SEWER	100%
DRAINAGE	100%
WATER	100%
PAVEMENT	100%
SIDEWALKS	90%

CURRENT WORK

Sidewalk restoration is underway towards the intersection of St. Philip & Decatur. The brick sidewalk is first, and the slate will be second. Fencing has been decreased along the block with more reduction expected in the next week.

900 DECATUR

St. Philip to Dumaine

ESTIMATED COMPLETION
Fall 2026

SEWER	100%
DRAINAGE	100%
WATER	100%
PAVEMENT	75%
SIDEWALKS	0%

CURRENT WORK

Crews are preparing the intersection of Dumaine & Decatur for the final concrete pour of the project. N. Peters was reopened to traffic last week. Both sides will close for a day next week for the final layer of asphalt. Notification will be given prior to the shutdown.

CURRENT CONSTRUCTION PHOTOS - PROVIDED IN SWBNO'S OCTOBER 27TH UPDATE




600 St. Peter



1100 Decatur



1000 Decatur

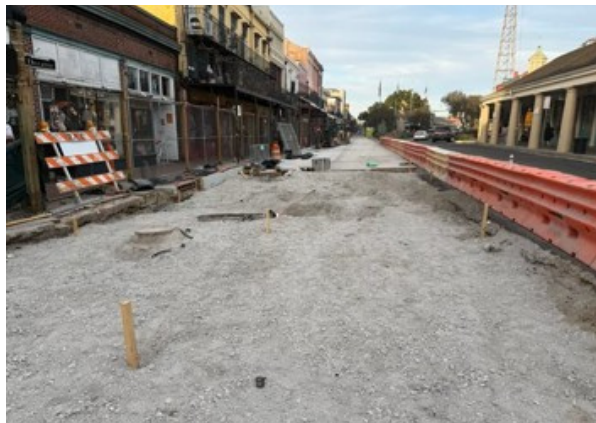

900 Decatur

SOURCE: SWBNO TM010 UPDATE - OCTOBER 27, 2026

This visual does not calculate or imply an overall project-completion percentage.
