



FRENCH QUARTER CONSTRUCTION UPDATE

600 St Peter St and 900-1100 Decatur St

Updated
September 2, 2026

600 ST. PETER

Chartres to Royal

ESTIMATED COMPLETION
Summer 2026

SEWER	100%
DRAINAGE	100%
WATER	100%
PAVEMENT	98%
SIDEWALKS	95%

CURRENT WORK

SWBNO & Roubion have completed the street repair from the Cox damage. The sidewalk restoration in front of the damaged area started today. Crews are currently finishing sidewalk restoration at the corner of Royal & St. Peter. The roadway will be paved after sidewalk completion.

1100 DECATUR

Gov. Nicholls to Ursulines

ESTIMATED COMPLETION
Summer 2026

SEWER	100%
DRAINAGE	100%
WATER	100%
PAVEMENT	100%
SIDEWALKS	99%

CURRENT WORK

Roubion crews have completed asphalt operations for this block. SWBNO will be walking this block for punch list items once final details are completed for this block. Striping the roadway for this block is up next.

1000 DECATUR

Ursulines to St. Philip

ESTIMATED COMPLETION
Fall 2026

SEWER	100%
DRAINAGE	100%
WATER	100%
PAVEMENT	95%
SIDEWALKS	60%

CURRENT WORK

Sidewalk restoration on the river side (slate) is complete. Roubion crews are working on the brick sidewalk on the lake side of the street up to the tie in point. This area will be the next to have fencing removed.

900 DECATUR

St. Philip to Dumaine


ESTIMATED COMPLETION
Fall 2026

SEWER	100%
DRAINAGE	100%
WATER	100%
PAVEMENT	10%
SIDEWALKS	0%

CURRENT WORK

The final waterline tie-in for this project is complete. All underground utilities are now complete. Restoration crews are working on roadway restoration for this final portion of the project. They are currently installing base course and geofabric for the roadway.

CURRENT CONSTRUCTION PHOTOS - PROVIDED IN SWBNO'S SEPTEMBER 2ND UPDATE

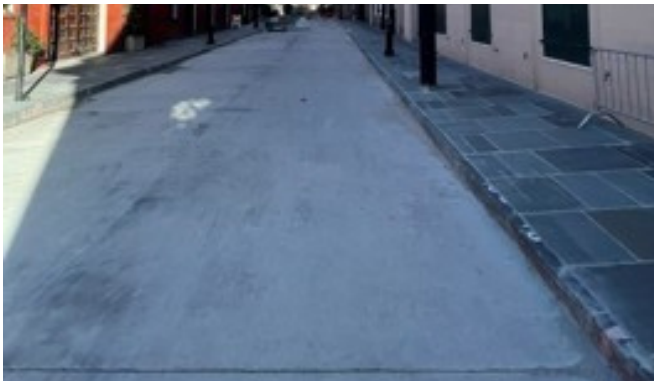

600 St. Peter



1100 Decatur



1000 Decatur



900 Decatur

SOURCE: SWBNO TM010 UPDATE - SEPTEMBER 2, 2026

This visual does not calculate or imply an overall project-completion percentage.
