



FRENCH QUARTER CONSTRUCTION UPDATE

600 St Peter St and 900-1100 Decatur St

Updated
September 24, 2026

600 ST. PETER

Chartres to Royal

ESTIMATED COMPLETION
September 2026

SEWER	100%
DRAINAGE	100%
WATER	100%
PAVEMENT	97%
SIDEWALKS	100%

CURRENT WORK

Asphalt installation is complete for this block. There is still remaining work on this block that must be completed prior to reopening. This work includes striping, saw cutting, cleanup, and final inspection. (Pavement completion percentage reflected above)

1100 DECATUR

Gov. Nicholls to Ursulines

ESTIMATED COMPLETION
Summer 2026

SEWER	100%
DRAINAGE	100%
WATER	100%
PAVEMENT	97%
SIDEWALKS	100%

CURRENT WORK

Roubion crews have completed asphalt operations for this block. SWBNO will be walking this block for punchlist items once final details are completed for this block. Striping for this block is up next. This block will remain closed for vehicular traffic for the duration of the project for safety. (Pavement completion percentage reflected above)

1000 DECATUR

Ursulines to St. Philip

ESTIMATED COMPLETION
Fall 2026

SEWER	100%
DRAINAGE	100%
WATER	100%
PAVEMENT	95%
SIDEWALKS	80%

CURRENT WORK

Sidewalk restoration is mostly complete beyond mid-block. Concrete poured 9/24 at Decatur and St. Philip.

900 DECATUR

St. Philip to Dumaine

ESTIMATED COMPLETION
Fall 2026

SEWER	100%
DRAINAGE	100%
WATER	100%
PAVEMENT	15%
SIDEWALKS	0%

CURRENT WORK

Crews continued installing rock base and installing curb along this block. Once curb installation is complete, the roadway will be formed and prepped for concrete. Entergy to be on site in the next few days to adjust their manholes.


CURRENT CONSTRUCTION PHOTOS - PROVIDED IN SWBNO'S SEPTEMBER 24TH UPDATE



600 St. Peter



1100 Decatur

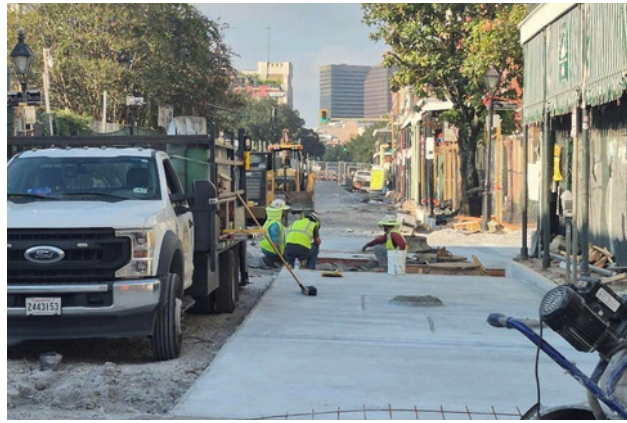

1000 Decatur



900 Decatur

SOURCE: SWBNO TM010 UPDATE - SEPTEMBER 24, 2026

This visual does not calculate or imply an overall project-completion percentage.
